Detour Signing Diagram
Snell Road Culvert #52623

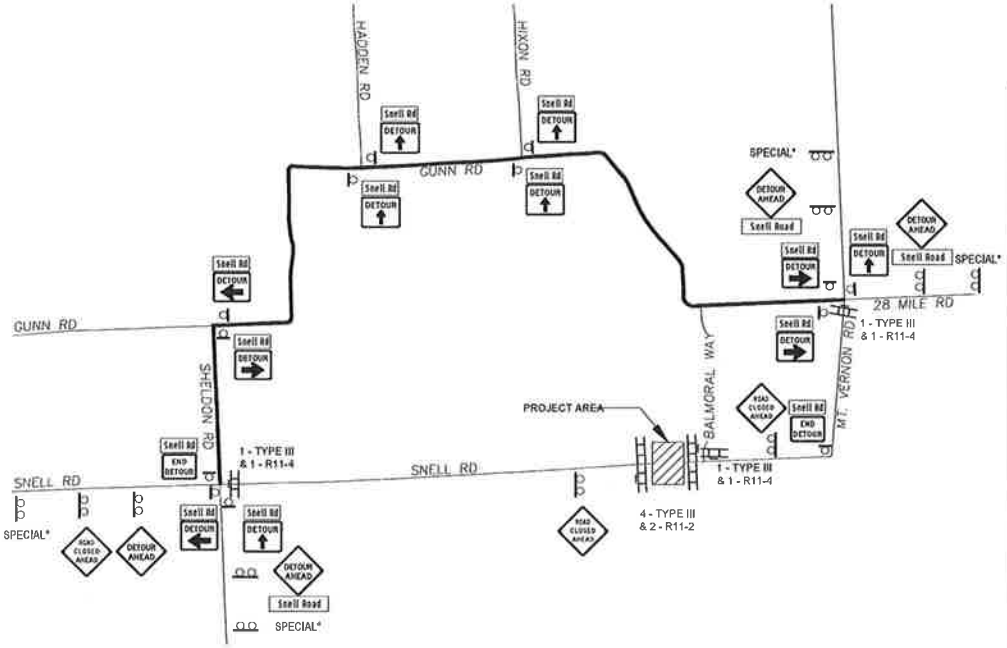

SIGNS TO BE REMOVED WITH PROJECT

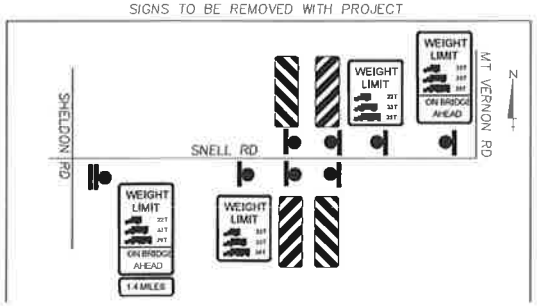

N

FULL SIZE (22"X34") NTS
REDUCED SIZE (11"X17") NTS

Know what's below. Call before you dig.

*SIGNING FABRICATION DETAILS

D3-2*

Snell Road

No border, White on Orange;
[Snell Road] Black Clearview-Hwy-1-W;

D3-1*

Snell Rd

No border, White on Orange;
[Snell Rd] Black Clearview-Hwy-1-W specified length;

SPECIAL*

Snell Road Closed
Sheldon Rd to Mt Vernon
Follow Detour

Starting XX/XX/XX

TRAFFIC DEVICES THIS SHEET		
ITEM	UNIT	QTY
Sign, Type B, Temp, Prismatic, Furn	Sft	228.5
Sign, Type B, Temp, Prismatic, Oper	Sft	228.5
Sign, Type B, Temp, Prismatic, Special, Furn	Sft	172.5
Sign, Type B, Temp, Prismatic, Special, Oper	Sft	172.5
Barricade, Type III, High Intensity, Double Sided, Lighted, Furn	Ea	7
Barricade, Type III, High Intensity, Double Sided, Lighted, Oper	Ea	7
Sign, Type III, Rem	Ea	9

KEY

4	SPECIAL*	Snell Road Closed Sheldon Rd to Mt Vernon Follow Detour / Starting XX/XX/XX

SPECIALS TO BE INSTALLED 2 WEEKS PRIOR TO CONSTRUCTION

3	W20-2-48	ROAD CLOSED AHEAD
4	W20-2-48	DETOUR AHEAD
3	D3-2*	Snell Road
13	D3-1*	Snell Rd
2	M4-8A-30	END DETOUR
3	M4-9-30 R	DETOUR
6	M4-9-30 T	DETOUR
2	M4-9-30 L	DETOUR

EACH M4-9 SHALL HAVE A D3-1 ROAD NAME PLAQUE.

2	R11-2	ROAD CLOSED
3	R11-4	ROAD CLOSED TO THRU TRAFFIC
7	TYPE III	

DETOUR ROUTE

ROAD COMMISSION OF OAKLAND COUNTY, BEVERLY HILLS, MICHIGAN	PROJECT NO. 52623 / DATE 07/18/17	TRAFFIC DETOUR / SNELL ROAD OVER MCCLURE DRAIN	DESIGN PHASE FINAL PLANS / SHEET NO. 6 OF 21

T:\PROJECTS\52623 - SNELL ROAD OVER MCCLURE DRAIN\P-AN PRODUCTION\MASTER PLANS\SSD - DETOUR SHEET JUL 18, 17 - 2:33 PM
