PROJECT NO. 53904 PROJECT NAME: 2018 BRIDGE PREVENTATIVE MAINTENANCE PROJECT

Traffic Safety Secord Lake Rd Detour Signing Diagram

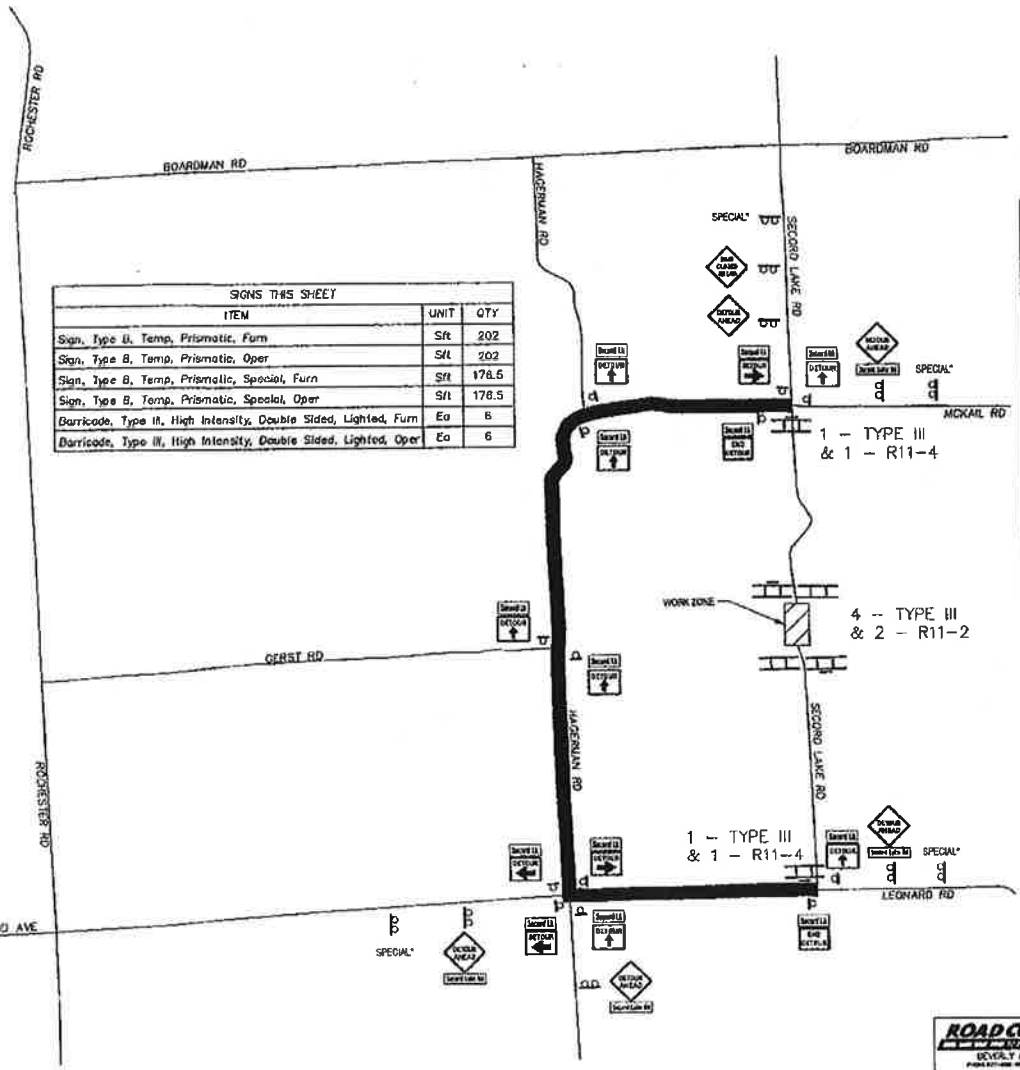

SIGNS THIS SHEET		
ITEM	UNIT	QTY
Sign, Type B, Temp, Prismatic, Furn	Sft	202
Sign, Type B, Temp, Prismatic, Oper	Sft	202
Sign, Type B, Temp, Prismatic, Special, Furn	Sft	178.5
Sign, Type B, Temp, Prismatic, Special, Oper	Sft	178.5
Barricade, Type III, High Intensity, Double Sided, Lighted, Furn	Ea	6
Barricade, Type III, High Intensity, Double Sided, Lighted, Oper	Ea	6

*SIGNING FABRICATION DETAILS

SPECIAL*

Secord Lk Rd Closed
Leonard Rd to
Mc Kail Road
Follow Detour

Starting XX/XX/XX

D3-2*

Secord Lake Rd

No border, White on Orange;
(Secord Lake Rd) Black 6 specified length;

D3-1*

Secord Lk

No border, White on Orange;
(Secord Lk) Black 6 specified length;

KEY

4	SPECIAL*	Secord Lk Rd Closed Leonard Rd to Mc Kail Road Follow Detour Starting XX/XX/XX

SPECIALS TO BE INSTALLED 2 WEEKS PRIOR TO CONSTRUCTION

1	W20-2-48	ROAD CLOSED AHEAD
5	W20-2-48	DETOUR AHEAD
4	D3-2*	Secord Lake Rd
13	D3-1*	Secord Lk
2	M4-9A-30	END DETOUR
2	M4-9-30 R	DETOUR
7	M4-9-30 T	DETOUR
2	M4-9-30 L	DETOUR

EACH M4-9 SHALL HAVE A D3-1 ROAD NAME PLAQUE.

2	R11-2	ROAD CLOSED
2	R11-4	ROAD CLOSED TO THRU TRAFFIC
6	TYPE III	

DETOUR ROUTE

WORK ZONE

ROAD COMMISSION OAKLAND COUNTY DEVELOPMENT DIVISION, DEVONSHIRE HILLS, MICHIGAN	PROJECT NO. 53904 DATE 03/16/2018	SECORD LK BRIDGE DETOUR 2018 BRIDGE PREVENTATIVE MAINTENANCE PROJECT	DESIGN PHASE FINAL PLAN SHEET NO. 8 OF 51

CONTROL SECTION 63900 REDOT JOB NO. 133507A & 133221A

PROJECT NAME: 2018 BRIDGE PREVENTATIVE MAINTENANCE PROJECT ROAD TO ROAD

PROJECT NO. 53904 SQUAD NO. SQUAD #1

T:\PROJECTS\53904-53904-53904 - 2018 BRIDGE PAVEMENT PREVENTATIVE SAFETY\TRAFFIC SAFETY\53904 T-5 DETOUR Apr 23, 19 - 1:50 PM
